



PROJECT: CBFH

PROGRESS REPORT

REPORT DATE

Date 3/29/2024

PREPARED BY

Name Al Banks

PROJECT OVERVIEW

ACTIVITY DESCRIPTION/PICTURE



Apparatus Bay w/ trench drain prep.

ACTIVITY DESCRIPTION/PICTURE




Change – trench drain with VB and rebar.



15-mil VP installation.



Rebar install complete and inspected.

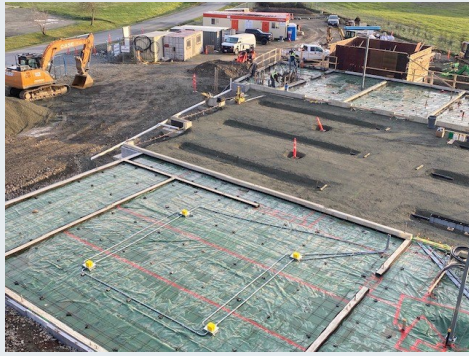

General overview – March 22nd.



General overview – March 22nd.



General overview – March 28th.



Tank location prepped.



Stair tower formwork for 2nd level.



Rebar zone flying into stair tower

FORECAST (UPCOMING WEEK'S)

- *SOG between GL 1.1/1.2 & 1.5/1.6 will be poured.*
- *Apparatus Bay trench drain installation will continue.*
- *The stair/hose tower formwork will continue.*
