



PROJECT: CBFH

PROGRESS REPORT

REPORT DATE

Date 7/26/2024

PREPARED BY

Name Steve Ziehr

PROJECT OVERVIEW

ACTIVITY DESCRIPTION/PICTURE



Wall membrane progressing East


ACTIVITY DESCRIPTION/PICTURE



Wall membrane progressing North



Aluminum frames and vinyl window mockup progressing

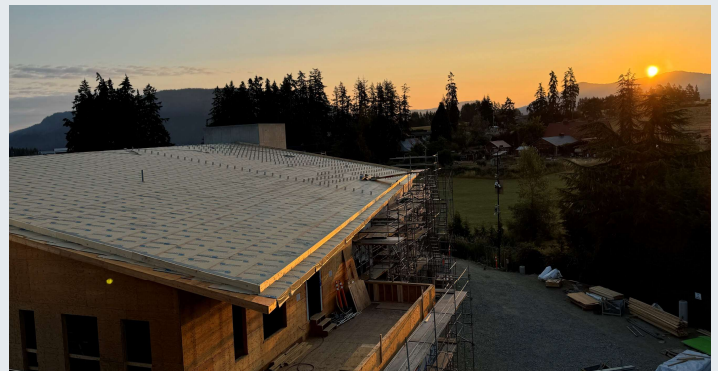

Roof VB complete / steel beam in / insulation clips started



Hose tower stair pre-fab started



Envelope access scaffold on West progressing



L1 South ceiling insulation complete / drywall commenced



L2 North sprinkler installation commenced



L2 South interior framing near complete



Roof insulation onsite.

FORECAST (UPCOMING 2 WEEKS)

- All framing completing. Interior insulation and pre-board progressing.
- Mechanical and Electrical rough-in continues, commencing in apparatus bay.
- Starline Window install, exterior aluminum frame install, steel stair structure, roofing and exterior wall insulation
